

Soil Erosion and Sediment Control Plan

For:

20 Goddard Drive Warehouse

20 Goddard Drive

Cranston, Rhode Island

Assessor's Plat 13, Lot 39

Owner:

20 Goddard, LLC
10 Greene Street
Providence, RI 02903
401-273-8010

Operator:

*TO BE DETERMINED UPON
CONTRACT AWARD*

OPERATOR NAME
STREET ADDRESS
CITY/TOWN, STATE ZIP
PHONE NUMBER

Estimated Project Dates:

Start Date: Spring 2023
Completion Date: Spring 2025

SESC Plan Prepared By:

Garofalo and Associates, Inc.
Samuel Hemenway, PE.
85 Corliss Street, P.O. Box 6145
Providence, Rhode Island 02904
(401) 273-6000
shemenway@garofaloassociates.com
RI Professional Engineer License Number: 6349

**SESC Plan
Preparation Date:**

May 25, 2022

**SESC Plan Revision
Date:**

OPERATOR CERTIFICATION

I certify under penalty of law that this document and all attachments were prepared under the direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that it is the responsibility of the owner/operator to implement and amend the Soil Erosion and Sediment Control Plan as appropriate in accordance with the requirements of the RIPDES Construction General Permit.

Operator Signature:

Date

Contractor Representative: Name

Contractor Title: Title

Contractor Company Name: Company Name (if applicable)

Address: Mailing Address

Phone Number: Phone Number

Email Address: Email

TABLE OF CONTENTS

OPERATOR CERTIFICATION.....	2
TABLE OF CONTENTS	3
INTRODUCTION.....	4
ADDITIONAL RESOURCES	4
SECTION 1: SITE DESCRIPTION.....	4
1.1 Project/Site Information.....	4
1.3 Natural Heritage Area Information	5
1.4 Historic Preservation/Cultural Resources	6
SECTION 2: EROSION, RUNOFF, AND SEDIMENT CONTROL.....	6
2.1 Avoid and Protect Sensitive Areas and Natural Features	6
2.2 Minimize Area of Disturbance	7
2.3 Minimize the Disturbance of Steep Slopes	8
2.4 Preserve Topsoil.....	8
2.5 Stabilize Soils	8
2.6 Protect Storm Drain Outlets.....	9
2.7 Establish Temporary Controls for the Protection of Post-Construction Stormwater Treatment Practices	10
2.8 Divert or Manage Run-on from Up-gradient Areas	10
2.9 Retain Sediment Onsite through Structural and Non-Structural Practices	10
2.10 Properly Design Constructed Stormwater Conveyance Channels.....	13
2.11 Erosion, Runoff, and Sediment Control Measure List.....	14
SECTION 3: CONSTRUCTION ACTIVITY POLLUTION PREVENTION.....	15
3.1 Existing Data of Known Discharges from Site.....	15
3.2 Prohibited Discharges.....	15
3.3 Proper Waste Disposal	16
3.4 Spill Prevention and Control	16
3.5 Control of Allowable Non-Stormwater Discharges	17
3.6 Control Dewatering Practices	18
3.7 Establish Proper Building Material Staging Areas.....	18
3.8 Minimize Dust	18
3.9 Designate Washout Areas	19
3.10 Establish Proper Equipment/Vehicle Fueling and Maintenance Practices	19
3.11 Chemical Treatment for Erosion and Sediment Control.....	19
3.12 Construction Activity Pollution Prevention Control Measure List.....	21
SECTION 4: CONTROL MEASURE INSTALLATION, INSPECTION, and MAINTENANCE	22
4.1 Installation.....	22
4.2 Monitoring Weather Conditions.....	22
4.3 Inspections.....	22
4.4 Maintenance	23
4.5 Corrective Actions.....	24
SECTION 5: AMENDMENTS.....	24
SECTION 6: RECORDKEEPING	25
SECTION 7: PARTY CERTIFICATIONS.....	26
LIST OF ATTACHMENTS.....	27

INTRODUCTION

The purpose of erosion, runoff, and sedimentation control measures is to prevent pollutants from leaving the construction site and entering waterways or environmentally sensitive areas during and after construction. This SESC Plan has been prepared prior to the initiation of construction activities to address anticipated worksite conditions. The control measures depicted on the site plan and described in this narrative should be considered the minimum measures required to control erosion, sedimentation, and stormwater runoff at the site. Since construction is a dynamic process with changing site conditions, it is the operator's responsibility to manage the site during each construction phase so as to prevent pollutants from leaving the site. This may require the operator to revise and amend the SESC Plan during construction to address varying site and/or weather conditions, such as by adding or realigning erosion or sediment controls to ensure the SESC Plan remains compliant with the RIPDES Construction General Permit. Records of these changes must be added to the amendment log attached to the SESC Plan, and to the site plans as "red-lined" drawings. Please Note: **Even if practices are correctly installed on a site according to the approved plan, the site is only in compliance when erosion, runoff, and sedimentation are effectively controlled throughout the entire site.**

It is the responsibility of the site owner and the site operator to maintain the SESC Plan at the site, including all attachments, amendments and inspection records, and to make all records available for inspection by RIDEM during and after construction. (RIPDES CGP - Part III.G)

The site owner, the site operator, and the designated site inspector are required to review the SESC Plan and sign the Party Certification pages (Section 8). The primary contractor (if different) and all subcontractors (if applicable) involved in earthwork or exterior construction activities are also required to review the SESC Plan and sign the certification pages before construction begins.

Any questions regarding the SESC Plan, control measures, inspection requirements, or any other facet of this document may be addressed to the RIDEM Office of Water Resources, at 401-222-4700 or via email: water@dem.ri.gov.

SECTION 1: SITE DESCRIPTION

1.1 *Project/Site Information*


Project/Site Name: **20 Goddard Drive Warehouse**

The proposed development primarily involves the construction of an industrial warehouse. The central site access will be removed, and the northern and southern site entrances will each be reconstructed in close proximity to their existing locations. An employee parking field will be located along the northern side of the warehouse, and truck loading and storage facilities along with an additional row of parking spaces will be located along the southern side of the building. The development will provide landscaping improvements, and will include associated pedestrian features, walkways, lighting and other amenities.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

Project Street/Location:

- 20 Goddard Drive, Cranston RI

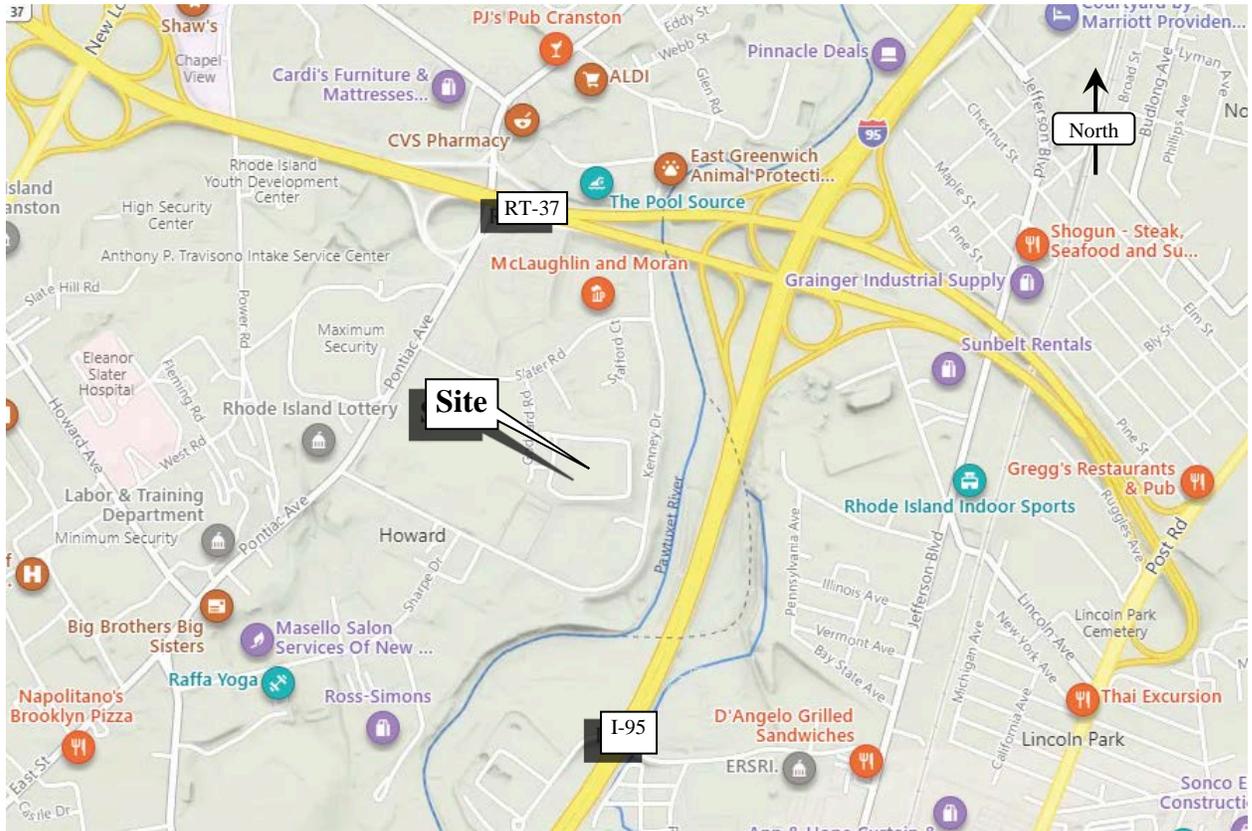

The following are estimates of the construction site area:

- Total Project Parcel Area 16.84 acres
- Total Project Area to be Disturbed 16.84 acres

Yes No The Limits of Disturbance have been marked in the field

1.3 Natural Heritage Area Information

RIPDES CGP - Part III.H

RIDEM Rhode Island Natural Heritage Program <mailto:plan@dem.ri.gov>

Are there any Natural Heritage Areas being disturbed by the construction activity or will discharges be directed to the Natural Heritage Area as a result of the construction activity?

Yes No

If yes, describe or refer to documentation which determines the likelihood of an impact on this area and the steps that will be taken to address any impacts.

- RIDEM Environmental Resource Mapping

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

1.4 Historic Preservation/Cultural Resources

Are there any historic properties, historic cemeteries or cultural resources on or near the construction site?

Yes No

Describe how this determination was made and summarize state or tribal review comments:

- RIDEM Environmental Resource Mapping

If yes, describe or refer to documentation which determines the likelihood of an impact on this historic property, historic cemetery or cultural resource and the steps taken to address that impact including any conditions or mitigation measures that were approved by other parties.

SECTION 2: EROSION, RUNOFF, AND SEDIMENT CONTROL

RIPDES Construction General Permit – Part III.J.1 – Erosion, Runoff, and Sediment Controls

The purpose of erosion controls is to prevent sediment from being detached and moved by wind or the action of raindrop, sheet, rill, gully, and channel erosion. Properly installed and maintained erosion controls are the primary defense against sediment pollution.

Runoff controls are used to slow the velocity of concentrated water flows. By intercepting and diverting stormwater runoff to a stabilized outlet or treatment practice or by converting concentrated flows to sheet flow erosion and sedimentation are reduced.

Sediment controls are the last line of defense against moving sediment. The purpose is to prevent sediment from leaving the construction site and entering environmentally sensitive areas.

This section describes the set of control measures that will be installed before and during the construction project to avoid, mitigate, and reduce impacts associated with construction activity. Specific control measures and their applicability are contained in Section Four: Erosion Control Measures, Section Five: Runoff Control Measures, and Section Six: Sediment Control Measures of the RI SESC Handbook. The RI SESC Handbook can be found at the following address:

<http://www.dem.ri.gov/soilerosion2014final.pdf>

2.1 Avoid and Protect Sensitive Areas and Natural Features

Areas of existing and remaining vegetation and areas that are to be protected as identified in the Section 1.6 of the SESC Plan must be clearly identified on the SESC Site Plans for each Phase of Construction. Prior to any land disturbance activities commencing on the site, the Contractor shall physically mark limits of disturbance (LOD) on the site and any areas to be protected within the site, so that workers can clearly identify the areas to be protected.

Feature Requiring Protection	Construction Phase #	Method of Protection	Sheet #
All areas adjacent to the construction activities shall be protected, with particular attention toward adjacent stormwater management facilities and storm drains	All Phases	Silt Sock / Silt Fence, catch basin inlet protection, construction access	C-4

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

2.2 Minimize Area of Disturbance

Will >5 acres be disturbed in order to complete this project?

Yes No

Will <5 acres be disturbed or will disturbance activities be completed within a six (6) month window?

Yes No

Sequencing of work areas is anticipated during all phases to minimize area of disturbance.

Based on the answers to the above questions will phasing be required for this project?

Yes No

16.84 acres to be disturbed.

PHASING PLAN

The following are estimates of each phase of the construction project:

Proper sequencing of construction activities is essential to maximize the effectiveness of erosion, runoff, and sediment control measures. Construction sequencing and timing of construction activities will include:

- Phase 1 - BEFORE DEMOLITION/EARTHWORK

Total Area of Phase	16.84 acres
Area to be Disturbed	16.84 acres

- Survey and stake the drainage structures, limit of disturbance, and sedimentation barriers.
- Install Construction Entrances
- Place sedimentation barriers (hay bales or silt sock) and silt sacks.
- Construct Material Stockpile area, Truck Wash-out, and Truck Refueling areas.

- Phase 2 - DURING DEMOLITION/EARTHWORK

- Total Area of Phase 16.84 acres
- Area to be Disturbed 16.84 acres

- Pavement removal.
- Construct Diversions and Temporary Sediment Traps/Basins.
- Sedimentation control structures shall be inspected and maintained promptly after rain event.
- Place sedimentation barriers (hay bales or silt sock) and silt sacks adjacent to utility corridors and on new drainage structures immediately after installation.
- Hay bales and/or silt sock shall be located as conditions warrant or as directed by the Engineer.
- Hay bales and/or silt sock sediment storage structure/pond.
- Protect planned infiltration sites and/or qualifying pervious areas (QPA's) from compaction.
- Denuded areas shall be seeded and all disturbed slopes shall be treated with hay, straw, or fiber mulch.

- Phase 3 - FINAL STABILIZATION

- Total Area of Phase 16.84 acres
- Area to be Disturbed 16.84 acres

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

- Pavement aggregate base to stabilized subgrade.
- Temporary erosion and sedimentation control, hay bales and/or silt socks, shall be removed following vegetative establishment on all disturbed areas.

2.3 Minimize the Disturbance of Steep Slopes

Are steep slopes (>15%) present within the proposed project area?

Yes No

- Steep slopes (>15%) are present along northern, eastern and southern areas within the project area. The proposed design has minimized disturbance/alteration of these areas to the maximum extent practicable, however all banks and slopes >5% shall be seeded as soon as possible and shall be protected with a hay, straw or fiber mulch as noted on the *Soil Erosion and Sediment Control Site Plan* (Plan C-4).

2.4 Preserve Topsoil

Site owners and operators must preserve existing topsoil on the construction site to the maximum extent feasible and as necessary to support healthy vegetation, promote soil stabilization, and increase stormwater infiltration rates in the post-construction phase of the project.

Will existing topsoil be preserved at the site?

Yes No

- Topsoil shall be stripped and stockpiled for re-use. Material Stockpile Zones are identified on the *Soil Erosion and Sediment Control Site Plan* and shall be protected with linear erosion controls and stabilized in accordance with this plan. (Plan C-4)

Soil compaction must be minimized by maintaining limits of disturbance throughout construction. In instances where site soils are compacted the site owner and operator must restore infiltration capacity of the compacted soils by tilling or scarifying compacted soils and amending soils as necessary to ensure a minimum depth of topsoil is available in these areas. In areas where infiltrating stormwater treatment practices are located compacted soils must be amended such that they will comply the design infiltration rates.

- Future Infiltration Zones are identified on the *Soil Erosion and Sediment Control Site Plan* (C-4). The contractor is asked to minimize construction activity that includes heavy equipment within these zones and they are to protect the zones through the construction process.

2.5 Stabilize Soils

Upon completion and acceptance of site preparation and initial installation of erosion, runoff, and sediment controls and temporary pollution prevention measures, the operator shall initiate appropriate temporary or permanent stabilization practices during all phases of construction on all disturbed areas as soon as possible, but not more than fourteen (14) days after the construction activity in that area has temporarily or permanently ceased.

Any disturbed areas that will not have active construction activity occurring within 14 days must be stabilized using the control measures depicted in the SESC Site Plans, in accordance with the *RI SESC Handbook*, and per manufacturer product specifications.

Only areas that can be reasonably expected to have active construction work being performed within 14 days of disturbance will be cleared/grubbed at any one time. It is NOT acceptable to clear and grub the entire construction site if portions will not be active within the 14-day time frame. Proper phasing of clearing

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

and grubbing activities shall include temporary stabilization techniques for areas cleared and grubbed that will not be active within the 14-day time frame.

All disturbed soils exposed prior to October 15 of any calendar year shall be seeded by that date if vegetative measures are the intended soil stabilization method. Any such areas that do not have adequate vegetative stabilization, as determined by the site operator or designated inspector, by November 15, must be stabilized through the use of non-vegetative erosion control measures. If work continues within any of these areas during the period from October 15 through April 15, care must be taken to ensure that only the area required for that day's work is exposed, and all erodible soil must be re-stabilized within 5 working days. In limited circumstances, stabilization may not be required if the intended function of a specific area of the site necessitates that it remains disturbed (i.e. construction of a motocross track).

Temporary Vegetative Control Measures

- Temporary vegetative cover will be established using hydro-seeding for areas of exposed soil, including stockpiles where construction activity will cease for more than 15 days.
- The use of temporary vegetative control shall occur in areas that have slopes steeper than 3:1 and for areas of temporary stockpiles that have not been used within 30 days.

Temporary Non-Vegetative Control Measures

- The use of a temporary sediment basin will be used on the site as a sediment control measure during construction.
- Silt sock / Silt Fence siltation barrier will be installed to collect all sediment suspended in storm water runoff.
- Organic mulch will be applied to exposed soils during short periods of construction.
- Dust from the site will be controlled by applying potable water to disturbed areas.
- Immediately after formation of final grades install erosion control matting as detailed.

Permanent Vegetative Control Measures

- Paving and other site improvements will provide permanent stabilization for the project.
- Landscape plant material.

Permanent Non-Vegetative Control Measures

- All areas of disturbance will have permanent vegetative control measures. Seeding of slopes will be with non-invasive plant materials.
- Rolled erosion control matting for steep slopes (>3:1).

2.6 Protect Storm Drain Outlets

Temporary or permanent outlet protection must be used to prevent scour and erosion at discharge points through the protection of the soil surface, reduction in discharge velocities, and through the promotion of infiltration. Outlets often have high velocity, high volume flows, and require strong materials that will withstand the forces of stormwater. Storm drain outlet control measures also offer a last line of protection against sediment entering environmentally sensitive areas.

All stormwater outlets that may discharge sediment-laden stormwater flow from the construction site must be protected using the control practices depicted on the approved plan set and in accordance with the *RI SESC Handbook*.

Will temporary or permanent point source discharges be generated at the site as the result of construction of sediment traps or basins, diversions, and conveyance channels?

Yes No

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

2.7 Establish Temporary Controls for the Protection of Post-Construction Stormwater Treatment Practices

Temporary measures shall be installed to protect permanent or long-term stormwater control and treatment measures as they are installed and throughout the construction phase of the project so that they will function properly when they are brought online.

Will long-term stormwater treatment practices be installed at the site?

Yes No

- Two (2) BMPs (Lined Surface Sand Filter and Infiltration/Detention Basin) will be installed on the site. Details are included in the Operation and Maintenance Manual.
- Soil Erosion and Sediment Control Site Plan (Plan C-4)

2.8 Divert or Manage Run-on from Up-gradient Areas

Is stormwater from off-site areas anticipated to flow onto the project area or onto areas where soils will be disturbed?

Yes No

Pre-Construction and Construction sub-watershed maps are included for each phase in this SESC Plan submittal.

Structural control measures will be used to limit stormwater flow from coming onto the project area, and to divert and slow on-site stormwater flow that is expected to impact exposed soils for the purpose of minimizing erosion, runoff, and the discharge of pollutants from the site.

Control measures shall be installed as depicted on the approved plan set and in accordance with the <i>RI SESC Handbook</i> or the <i>RI Department of Transportation Standard Specifications for Road and Bridge Construction</i> . Run-on and Run-off Management				
Construction Phase #	On-site or Off-site Run-on?	Control measure	Identified on Sheet #	Detail(s) is/are on Sheet #
All Phases	On-Site	Silt Sock/ Fence	C-4	C-4

2.9 Retain Sediment Onsite through Structural and Non-Structural Practices

SEDIMENT BARRIERS must be installed along the perimeter areas of the site that will receive stormwater from disturbed areas. This also may include the use of sediment barriers along the contour of disturbed slopes to maintain sheet flow and minimize rill and gully erosion during construction. Installation and maintenance of sediment barriers must be completed in accordance with the maintenance requirements specified by the product manufacturer or the *RI SESC Handbook*.

Will sediment barriers be utilized at the toe of slopes and other downgradient areas subject to stormwater impacts and erosion during construction?

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

Yes No

- Silt Sock and/or Silt Fence sediment protection is proposed at the downgradient position along the limit of proposed disturbance.

Will sediment barriers be utilized along the contour of slopes to maintain sheet flow and minimize rill and gully erosion during construction?

Yes No

- Because work will be continually performed within the limit of disturbance, barriers will only be specified for the limits.

SEDIMENT BARRIERS			
Construction Phase #	Sediment Barrier Type	Sediment Barrier is Labeled on Sheet #	Detail is on Sheet #
N/A	N/A	N/A	N/A

INLET PROTECTION will be utilized to prevent soil and debris from entering storm drain inlets. These measures are usually temporary and are implemented before a site is disturbed. ALL stormwater inlets and/or catch basins that are operational during construction and have the potential to receive sediment-laden stormwater flow from the construction site must be protected using control measures outlined in the *RI SESC Handbook*.

For more information on inlet protection refer to the *RI SESC Handbook*, Inlet Protection control measure.

Maintenance

The operator must clean, or remove and replace the inlet protection measures as sediment accumulates, the filter becomes clogged, and/or as performance is compromised. Accumulated sediment adjacent to the inlet protection measures should be removed by the end of the same work day in which it is found or by the end of the following work day if removal by the same work day is not feasible.

Do inlets exist adjacent to or within the project area that require temporary protection?

Yes No

The following lists the proposed storm drain inlet types selected from Section Six of the *RI SESC Handbook*. Each row is unique for each phase and inlet protection type.

INLET PROTECTION			
Construction Phase #	Inlet Protection Type	Inlet Protection is labeled on Sheet #	Detail(s) is/are on Sheet #
ALL	Silt Sack Catch Basin Protection	C-4	C-4

CONSTRUCTION ENTRANCES will be used in conjunction with the stabilization of construction roads to reduce the amount of sediment tracking off the project. This project has avoided placing construction entrances on poorly drained soils where possible. Where poorly drained soils could not be eliminated, the detail includes subsurface drainage.

Any construction site access point must employ the control measures on the approved SESC site plans and in accordance with the *RI SESC Handbook*. Construction entrances shall be used in conjunction with the stabilization of construction roads to reduce the amount of mud picked up by construction vehicles. All construction access roads shall be constructed prior to any roadway accepting construction traffic.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

The site owner and operator must:

1. Restrict vehicle use to properly designated exit points.
2. Use properly designed and constructed construction entrances at all points that exit onto paved roads so that sediment removal occurs prior to vehicle exit.
3. When and where necessary, use additional controls to remove sediment from vehicle tires prior to exit (i.e. wheel washing racks, rumble strips, and rattle plates).
4. Where sediment has been tracked out from the construction site onto the surface of off-site streets, other paved areas, and sidewalks, the deposited sediment must be removed by the end of the same work day in which the track out occurs. Track-out must be removed by sweeping, shoveling, or vacuuming these surfaces, or by using other similarly effective means of sediment removal.

Will construction entrances be utilized at the proposed construction site?

Yes No

CONSTRUCTION ENTRANCE			
Construction Phase #	Soil Type at the Entrance	Entrance is located on Sheet #	Detail is on Sheet #
All Phases	A	C-4	C-4

STOCKPILE CONTAINMENT will be used onsite to minimize or eliminate the discharge of soil, topsoil, base material or rubble, from entering drainage systems or surface waters. All stockpiles must be located within the limit of disturbance, protected from run-on with the use of temporary sediment barriers and provided with cover or stabilization to avoid contact with precipitation and wind where and when practical.

Stock pile management consists of procedures and practices designed to minimize or eliminate the discharge of stockpiled material (soil, topsoil, base material, rubble) from entering drainage systems or surface waters.

For any stockpiles or land clearing debris composed, in whole or in part, of sediment or soil, you must comply with the following requirements:

1. Locate piles within the designated limits of disturbance.
2. Protect from contact with stormwater (including run-on) using a temporary perimeter sediment barrier.
3. Where practicable, provide cover or appropriate temporary vegetative or structural stabilization to avoid direct contact with precipitation or to minimize sediment discharge.
4. NEVER hose down or sweep soil or sediment accumulated on pavement or other impervious surfaces into any stormwater conveyance, storm drain inlet, or surface water.
5. To the maximum extent practicable, contain and securely protect from wind.

STOCKPILE CONTAINMENT				
Construction Phase #	Run-on measures necessary? (yes/no)	Stabilization or Cover Type	Stockpile Containment Measure	Sheet #
All Phases	Yes	Cover as needed	Silt Sock	Sheet C-4

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

CONSTRUCTED SEDIMENT STRUCTURES

TEMPORARY SEDIMENT TRAPS will be utilized onsite. There will be no disturbed drainage areas greater than one acre that will be exposed for longer than six months. Design and sizing calculations in accordance with the *RI SESC Handbook*, Section Six are found in this SESC Plan. A summary of the calculations is provided below:

Are temporary sediment traps required at the site?

Yes No

TEMPORARY SEDIMENT BASIN(S) will be utilized onsite. Every effort must be made to prevent erosion.

Are temporary sediment basins required at the site?

Yes No

TEMPORARY SEDIMENT BASIN				
Construction Phase #	Exposed Area (acres)	Trap #	Sheet #	Detail found on Sheet#
ALL	16.84	1	C-4	C-5

- The project will expose areas greater than five (5) acres.

2.10 Properly Design Constructed Stormwater Conveyance Channels

Are temporary stormwater conveyance practices required in order to properly manage runoff within the proposed construction project?

Yes No

- Temporary ditches or dikes will be installed as required to direct stormwater runoff to the temporary sediment basin as noted on the *Soil Erosion and Sediment Control Site Plan* (Plan C-4).

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

2.11 Erosion, Runoff, and Sediment Control Measure List

It is expected that this table and corresponding Inspection Reports will be amended as needed throughout the construction project as control measures are added or modified.

All Phases			
Location/Station	Control Measure Description/Reference	Maintenance Requirement	Phase
Project Perimeter	Filter Socks	Sediment accumulated greater than half way up sock; break through or significant strain of barrier	All Phases
Construction Vehicle Entrances	Construction Access	Contractor shall assure that placed rip-rap remain.	All Phases
Construction Vehicle Entrances	Truck Washout	Silt Socks shall be monitored and assessed throughout operation.	All Phases
Truck Entrance	Truck Refueling	Silt Socks shall be monitored and assessed throughout operation.	All Phases
Site-wide	Dust Control	Provide dust control as warranted by weather and field conditions.	All Phases
Site Wide	Material Stockpile	Silt Socks shall be monitored and assessed throughout operation.	All Phases

SECTION 3: CONSTRUCTION ACTIVITY POLLUTION PREVENTION

The purpose of construction activity pollution prevention is to prevent day to day construction activities from causing pollution.

This section describes the key pollution prevention measures that must be implemented to avoid and reduce the discharge of pollutants in stormwater. Example control measures include the proper management of waste, material handling and storage, and equipment/vehicle fueling/washing/maintenance operations.

Where applicable, include *RI SESC Handbook* or the *RI Department of Transportation Standard Specifications for Road and Bridge Construction* (as amended) specifications.

3.1 Existing Data of Known Discharges from Site

Are there known discharges from the project area?

Yes No

Describe how this determination was made:

- Existing Conditions Survey

If yes, list discharges and locations:

A catch basin located within one of the existing parking facilities discharge to the existing closed drainage system within Goddard Drive.

Is there existing data on the quality of the known discharges?

Yes No

If yes, provide data:

- N/A

3.2 Prohibited Discharges

The following discharges are prohibited at the construction site:

- Contaminated groundwater, unless specifically authorized by the DEM. These types of discharges may only be authorized under a separate DEM RIPDES permit.
- Wastewater from washout of concrete, unless the discharge is contained and managed by appropriate control measures.
- Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction materials.
- Fuels, oils, or other pollutants used in vehicle and equipment operation and maintenance. Proper storage and spill prevention practices must be utilized at all construction sites.
- Soaps or solvents used in vehicle and equipment washing.
- Toxic or hazardous substances from a spill or other release.

All types of waste generated at the site shall be disposed of in a manner consistent with State Law and/or regulations.

Will any of the above listed prohibited discharges be generated at the site?

Yes No

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

Operation/ Location	Stormwater Pollutants
Clearing, grading, excavating, and un-stabilized areas	Sediment; Trash/Debris
Construction Entrance	Sediment
Soil Stockpiles	Sediment
Paving operations	Sediment; Trash/Debris
Concrete washout and waste	Heavy metals; pH; Trash/Debris
Structure construction/ painting/ cleaning	Nutrients; pH; Trash/Debris; Toxic chemicals
Material delivery and storage	Sediment; Nutrients; Heavy metals; pH; Pesticides/Herbicides; Oil/Grease; Trash/Debris; Toxic chemicals
Vehicle/equipment fueling and maintenance	Oil/Grease; Toxic chemicals
Landscaping operations	Sediment; Nutrients; Trash/Debris

3.3 Proper Waste Disposal

Building materials and other construction site wastes must be properly managed and disposed of in a manner consistent with State Law and/or regulations.

- A waste collection area shall be designated on the site that does not receive a substantial amount of runoff from upland areas and does not drain directly to a waterbody or storm drain.
- All waste containers shall be covered to avoid contact with wind and precipitation.
- Waste collection shall be scheduled frequently enough to prevent containers from overfilling.
- All construction site wastes shall be collected, removed, and disposed of in accordance with applicable regulatory requirements and only at authorized disposal sites.
- Equipment and containers shall be checked for leaks, corrosion, support or foundation failure, or other signs of deterioration. Those that are found to be defective shall be immediately repaired or replaced.

Is waste disposal a significant element of the proposed project?

Yes No

3.4 Spill Prevention and Control

All chemicals and/or hazardous waste material must be stored properly and legally in covered areas, with containment systems constructed in or around the storage areas. Areas must be designated for materials delivery and storage. All areas where potential spills can occur and their accompanying drainage points must be described. The owner and operator must establish spill prevention and control measures to reduce the chance of spills, stop the source of spills, contain and clean-up spills, and dispose of materials contaminated by spills. The operator must establish and make highly visible location(s) for the storage of spill prevention and control equipment and provide training for personnel responsible for spill prevention and control on the construction site.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

Are spill prevention and control measures required for this particular project?

Yes No

Spill Control Practices:

- Manufacturer's recommended methods shall be clearly posted for spill clean-up and site personnel shall be made aware of the procedures and the locations of clean-up information and supplies.
- Material and equipment necessary for spill clean-up will be kept on-site in a designated material storage area. Equipment will include, but not be limited to, brooms, dust pans, mops, rags, gloves, goggles, absorbent materials, sand, sawdust and plastic & metal trash containers specifically kept and labeled for this purpose.
- All spills will be cleaned-up immediately after discovery.
- Spills of toxic or hazardous materials or nature will be reported to the appropriate state, local or federal agency, as required by-law.
- The spill prevention plan will include provisions to adapt the plan to ensure that the spills will not reoccur, and how to clean up the spill if there is another one.
- Site operations and daily use shall consider the ultimate disposition of stormwater and other site-generated forms of runoff. Wash water with its combination of solvents, detergents and oil/greases should not be allowed to enter any part of the on-site drainage system.
- No vehicles will be left unattended in project areas, which in the event of a hazardous material spill, would flow into any portion of the drainage system.
- In the event of a release of hazardous material, the Contractor will take all measures to stop and/or contain the leak and without exacerbating the release, attempt to remove equipment from the areas likely to cause a discharge of hazardous materials into Water of the State. Further, site supervisors shall be contacted and, should it be determined that the spill is of reportable quantity, the State shall be notified. A licensed hazardous waste remediation contractor shall be engaged to remediate the spill in accordance with State Regulations and procedures.

3.5 Control of Allowable Non-Stormwater Discharges

Are there allowable non-Stormwater discharges present on or near the project area?

Yes No

List of allowable non-stormwater discharge(s) and the associated control measure(s):

- Truck Wash-out
- Truck refueling Area

Are there any known or proposed contaminated discharges, including anticipated contaminated dewatering operations, planned on or near the project area?

Yes No

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

3.6 Control Dewatering Practices

Site owners and operators are prohibited from discharging groundwater or accumulated stormwater that is removed from excavations, trenches, foundations, vaults, or other similar points of accumulation, unless such waters are first effectively managed by appropriate control measures.

Examples of appropriate control measures include, but are not limited to, temporary sediment basins or sediment traps, sediment socks, dewatering tanks and bags, or filtration systems (e.g. bag or sand filters) that are designed to remove sediment. Uncontaminated, non-turbid dewatering water can be discharged without being routed to a control.

At a minimum, the following discharge requirements must be met for dewatering activities:

1. Do not discharge visible floating solids or foam.
2. To the extent feasible, utilize vegetated, upland areas of the site to infiltrate dewatering water before discharge. In no case will surface waters be considered part of the treatment area.
3. At all points where dewatering water is discharged, utilize velocity dissipation devices.
4. With filter backwash water, either haul it away for disposal or return it to the beginning of the treatment process.
5. Replace and clean the filter media used in dewatering devices when the pressure differential equals or exceeds the manufacturer's specifications.
6. Dewatering practices must involve the implementation of appropriate control measures as applicable (i.e. containment areas for dewatering earth materials, portable sediment tanks and bags, pumping settling basins, and pump intake protection.)

Is it at all likely that the site operator will need to implement construction dewatering in order to complete the proposed project?

Yes No

3.7 Establish Proper Building Material Staging Areas

All construction materials that have the potential to contaminate stormwater must be stored properly and legally in covered areas, with containment systems constructed in or around the storage areas. Areas must be designated for materials delivery and storage. Designated areas shall be approved by the site owner/engineer. Minimization of exposure is not required in cases where the exposure to precipitation and to stormwater will not result in the discharge of pollutants, or where exposure of a specific material or product poses little risk of stormwater contamination (such as final products and materials intended for outdoor use).

- No chemicals of hazardous material shall be stored at the project site.

3.8 Minimize Dust

Dust control procedures and practices shall be used to suppress dust on a construction site during the construction process, as applicable. Precipitation, temperature, humidity, wind velocity and direction will determine amount and frequency of applications. However, the best method of controlling dust is to prevent dust production. This can best be accomplished by limiting the amount of bare soil exposed at one time.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

Dust Control measures outlined in the *RI SESC Handbook* shall be followed. Other dust control methods include watering, chemical application, surface roughening, wind barriers, walls, and covers.

- Applying water shall be utilized to minimize dust.

3.9 Designate Washout Areas

At no time shall any material (concrete, paint, chemicals) be washed into storm drains, open ditches, streets, streams, wetlands, or any environmentally sensitive area. The site operator must ensure that construction waste is properly disposed of, to avoid exposure to precipitation, at the end of each working day.

Will washout areas be required for the proposed project?

Yes No

- A truck wash-out area is proposed within the project site. The contractor is cautioned that all washing of trucks shall be performed within the designated area.

3.10 Establish Proper Equipment/Vehicle Fueling and Maintenance Practices

Vehicle fueling shall not take place within regulated wetlands or buffer zone areas, or within 50-feet of the storm drain system. Designated areas shall be depicted on the SESC Site Plans, or shall be approved by the site owner.

Vehicle maintenance and washing shall occur off-site, or in designated areas depicted on the SESC Site Plans or approved of by the site owner. Maintenance or washing areas shall not be within regulated wetlands or buffer zone areas, or within 50-feet of the storm drain system. Maintenance areas shall be clearly designated, and barriers shall be used around the perimeter of the maintenance area to prevent stormwater contamination.

Construction vehicles shall be inspected frequently for leaks. Repairs shall take place immediately. Disposal of all used oil, antifreeze, solvents and other automotive-related chemicals shall be according to applicable regulations; at no time shall any material be washed down the storm drain or in to any environmentally sensitive area.

- A truck refueling area is proposed within the project site. The contractor is cautioned that all truck refueling shall be performed within the designated area.

3.11 Chemical Treatment for Erosion and Sediment Control

Chemical stabilizers, polymers, and flocculants are readily available on the market and can be easily applied to construction sites for the purposes of enhancing the control of erosion, runoff, and sedimentation. The following guidelines should be adhered to for construction sites that plan to use treatment chemicals as part of their overall erosion, runoff, and sedimentation control strategy.

The U.S. Environmental Protection Agency has conducted research into the relative toxicity of chemicals commonly used for the treatment of construction stormwater discharges. The research conducted by the EPA focused on different formulations of chitosan, a cationic compound, and both cationic and anionic polyacrylamide (PAM). In summary, the studies found significant toxicity resulting from the use of chitosan and cationic PAM in laboratory conditions, and significantly less toxicity associated with using anionic PAM. EPA's research has led to the conclusion that the use of treatment chemicals for erosion, runoff, and sedimentation control requires proper operator training and appropriate usage to avoid risk to aquatic species. In the case of cationic treatment chemicals additional safeguards may be necessary.

Application/Installation Minimum Requirements

If a site operator plans to use polymers, flocculants, or other treatment chemicals during construction the SESC plan must address the following:

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

1. Treatment chemicals shall not be applied directly to or within 100 feet of any surface water body, wetland, or storm drain inlet.
2. Use conventional erosion, runoff, and sedimentation controls prior to and after the application of treatment chemicals. Use conventional erosion, runoff, and sedimentation controls prior to chemical addition to ensure effective treatment. Chemicals may only be applied where treated stormwater is directed to a sediment control (e.g. temporary sediment basin, temporary sediment trap or sediment barrier) prior to discharge.
3. Sites shall be stabilized as soon as possible using conventional measures to minimize the need to use chemical treatment.
4. Select appropriate treatment chemicals. Chemicals must be selected that are appropriately suited to the types of soils likely to be exposed during construction and to the expected turbidity, pH, and flow rate of stormwater flowing into the chemical treatment system or treatment area. **Soil testing is essential. Using the wrong form of chemical treatment will result in some form of performance failure and unnecessary environmental risk.**
5. Minimize discharge risk from stored chemicals. Store all treatment chemicals in leak-proof containers that are kept under storm-resistant cover and surrounded by secondary containment structures (e.g., spill berms, decks, spill containment pallets), or provide equivalent measures, designed and maintained to minimize the potential discharge of treatment chemicals in stormwater or by any other means (e.g., storing chemicals in covered areas or having a spill kit available on site).
6. Use chemicals in accordance with good engineering practices and specifications of the chemical provider/supplier. You must also use treatment chemicals and chemical treatment systems in accordance with good engineering practices, and with dosing specifications and sediment removal design specifications provided by the supplier of the applicable chemicals, or document specific departures from these practices or specifications and how they reflect good engineering practice.

Will chemical stabilizers, polymers, flocculants or other treatment chemicals be utilized on the proposed construction project?

Yes No

- Hydro-seeding
 1. The Contractor shall provide manufacturer's name and product name prior to application.
 2. The Contractor shall provide applicable Material Safety Data Sheets (MSDSs) or Safety Data Sheets (SDS) for hydro-seeding applications.
 3. The Contractor shall provide the results of third-party toxicity testing of the materials proposed for use at the site.
 4. The Contractor shall provide a certification from the site owner and operator that all proposed treatment chemicals are the same as those used in the toxicity tests and will not be altered in any way.
 5. The Contractor shall provide an explanation as to why conventional erosion, runoff, and sediment control measures, alone or in combination, will not be sufficient to prevent turbidity impacts and sedimentation in downstream receptors.
 6. The Contractor shall provide a plan prepared in consultation with the chemical treatment manufacturer(s) or authorized manufacturer's representative which includes the following:
 - a. Identification of the areas of the site where treatment chemicals will be applied and the name, location, and distance to all downstream receptors that have the potential to be impacted from the discharges from the treatment areas.
 - b. List the expected start and end dates or specific phases of the project during which each treatment chemical will be applied.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

- c. Provide test results for representative soils from the site, and any recommendations from the manufacturer based on the soil tests, indicating the type of treatment chemical and the recommended application rate.
- d. List the frequency, method, and rates of application which are designed to ensure that treatment chemical concentrations will not exceed 50% of the IC25 or NOEC toxicity values, whichever is less, for each treatment chemical proposed.
- e. Provide the frequency of inspection and maintenance of the treatment chemical application system.
- f. List the method proposed for the collection, removal, and disposal or stabilization of settled particles to prevent resuspension.
- g. Describe the training that will be provided to all persons who will handle and use treatment chemicals at the construction site. Training must include appropriate, product-specific training and proper dosing requirements for each product.

Treatment Chemical SESC Plan Weekly Inspection Report Documentation Requirements

- 1. Document the type and quantity of treatment chemicals applied.
- 2. List the date, duration of discharge, and estimated discharge rate.
- 3. Provide an estimate of the volume of water treated.
- 4. Provide an estimate of the concentration of treatment chemicals in the discharge, with supporting calculations.

3.12 Construction Activity Pollution Prevention Control Measure List

It is expected that this table will be amended as needed throughout the construction project.

Location/Station	Control Measure Description/Reference	Maintenance Requirement
Perimeter	Filter Socks	Sediment accumulated greater than half way up sock; break through or significant strain barrier
Truck Entrances	Construction Access	Contractor shall assure that placed rip-rap remain.
Truck Entrance	Truck Washout	Filter socks shall be monitored and assessed throughout operation
Truck Entrance	Truck Refueling	Filter Socks shall be monitored and assessed throughout operation
Site Wide	Material Stockpile	Filter Socks shall be monitored and assessed throughout operation

SECTION 4: CONTROL MEASURE INSTALLATION, INSPECTION, and MAINTENANCE

4.1 *Installation*

Complete the installation of temporary erosion, runoff, sediment, and pollution prevention control measures by the time each phase of earth-disturbance has begun. All stormwater control measures must be installed in accordance with good judgment, including applicable design and manufacturer specifications. Installation techniques and maintenance requirements may be found in manufacturer specifications and/or the *RI SESC Handbook*.

- Installation of temporary erosion, runoff, sediment, and pollution prevention control measures are identified on the *Soil Erosion and Sediment Control Site Plan* (Sheet C-4).

4.2 *Monitoring Weather Conditions*

Anticipating Weather Events - Care will be taken to the best of the operator's ability to avoid disturbing large areas prior to anticipated precipitation events. Weather forecasts must be routinely checked, and in the case of an expected precipitation event of over 0.25-inches over a 24-hour period, it is highly recommended that all control measures should be evaluated and maintained as necessary, prior to the weather event. In the case of an extreme weather forecast (greater than one-inch of rain over a 24-hour period), additional erosion/sediment controls may need to be installed.

Storm Event Monitoring For Inspections - At a minimum, storm events must be monitored and tracked in order to determine when post-storm event inspections must be conducted. Inspections must be conducted and documented at least once every seven (7) calendar days and within twenty-four (24) hours after any storm event, which generates at least 0.25 inches of rainfall per twenty-four (24) hour period and/or after a significant amount of runoff or snowmelt.

The weather gauge station and website that will be utilized to monitor weather conditions on the construction site is as follows:

8 Blaisdell Street, Cranston RI – KRICRANS40

<https://www.wunderground.com/weather/us/ri/cranston>

4.3 *Inspections*

Minimum Frequency - Each of the following areas must be inspected by or under the supervision of the owner and operator at least once every seven (7) calendar days and within twenty-four (24) hours after any storm event, which generates at least 0.25 inches of rainfall per twenty-four (24) hour period and/or after a significant amount of runoff or snowmelt:

- a. All areas that have been cleared, graded, or excavated and where permanent stabilization has not been achieved;
- b. All stormwater erosion, runoff, and sediment control measures (including pollution prevention control measures) installed at the site;
- c. Construction material, un-stabilized soil stockpiles, waste, borrow, or equipment storage, and maintenance areas that are covered by this permit and are exposed to precipitation;
- d. All areas where stormwater typically flows within the site, including temporary drainage ways designed to divert, convey, and/or treat stormwater;

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

- e. All points of discharge from the site;
- f. All locations where temporary soil stabilization measures have been implemented;
- g. All locations where vehicles enter or exit the site.

Reductions in Inspection Frequency - If earth disturbing activities are suspended due to frozen conditions, inspections may be reduced to a frequency of once per month. The owner and operator must document the beginning and ending dates of these periods in an inspection report.

Qualified Personnel – The site owner and operator are responsible for designating personnel to conduct inspections and for ensuring that the personnel who are responsible for conducting the inspections are “qualified” to do so. A “qualified person” is a person knowledgeable in the principles and practices of erosion, runoff, sediment, and pollution prevention controls, who possesses the skills to assess conditions at the construction site that could impact stormwater quality, and the skills to assess the effectiveness of any stormwater controls selected and installed to meet the requirements of the permit.

Recordkeeping Requirements - All records of inspections, including records of maintenance and corrective actions must be maintained with the SESC Plan. Inspection records must include the date and time of the inspection, and the inspector’s name, signature, and contact information.

General Notes

- A separate inspection report will be prepared for each inspection.
- The Inspection Reference Number shall be a combination of the RIPDES Construction General Permit No - consecutively numbered inspections. Example: Inspection reference number for the 4th inspection of a project would be: RIR10####-4
- Each report will be signed and dated by the Inspector and must be kept onsite.
- Each report will be signed and dated by the Site Operator.
- The corrective action log contained in each inspection report must be completed, signed, and dated by the site operator once all necessary repairs have been completed.
- It is the responsibility of the site operator to maintain a copy of the SESC Plan, copies of all completed inspection reports, and amendments as part of the SESC Plan documentation at the site during construction.

Failure to make and provide documentation of inspections and corrective actions under this part constitutes a violation of your permit and enforcement actions under 46-12 of R.I. General Laws may result.

4.4 Maintenance

Maintenance procedures for erosion and sedimentation controls and stormwater management structures/facilities are described on the SESC Site Plans and in the *RI SESC Handbook*.

Site owners and operators must ensure that all erosion, runoff, sediment, and pollution prevention controls remain in effective operating condition and are protected from activities that would reduce their effectiveness. Erosion, runoff, sedimentation, and pollution prevention control measures must be maintained throughout the course of the project.

Note: It is recommended that the site operator designates a full-time, on-site contact person responsible for working with the site owner to resolve SESC Plan-related issues.

Soil Erosion and Sediment Control Plan
20 Goddard Drive Warehouse

4.5 Corrective Actions

If, in the opinion of the designated site inspector, corrective action is required, the inspector shall note it on the inspection report and shall inform the site operator that corrective action is necessary. The site operator must make all necessary repairs whenever maintenance of any of the control measures instituted at the site is required.

In accordance with the *RI SESC Handbook*, the site operator shall initiate work to fix the problem immediately after its discovery, and complete such work by the close of the next work day, if the problem does not require significant repair or replacement, or if the problem can be corrected through routine maintenance.

When installation of a new control or a significant repair is needed, site owners and operators must ensure that the new or modified control measure is installed and made operational by no later than seven (7) calendar days from the time of discovery where feasible. If it is infeasible to complete the installation or repair within seven (7) calendar days, the reasons why it is infeasible must be documented in the SESC Plan along with the schedule for installing the control measures and making it operational as soon as practicable after the 7-day timeframe. Such documentation of these maintenance procedures and timeframes should be described in the inspection report in which the issue was first documented. If these actions result in changes to any of the control measures outlined in the SESC Plan, site owners and operators must also modify the SESC Plan accordingly within seven (7) calendar days of completing this work.

SECTION 5: AMENDMENTS

This SESC Plan is intended to be a working document. It is expected that amendments will be required throughout the active construction phase of the project. **Even if practices are installed on a site according to the approved plan, the site is only in compliance when erosion, runoff, and sedimentation are effectively controlled throughout the entire site for the entire duration of the project.**

The SESC Plan shall be amended within seven (7) days whenever there is a change in design, construction, operation, maintenance or other procedure which has a significant effect on the potential for the discharge of pollutants, or if the SESC Plan proves to be ineffective in achieving its objectives (i.e. the selected control measures are not effective in controlling erosion or sedimentation).

In addition, the SESC Plan shall be amended to identify any new operator that will implement a component of the SESC Plan.

All revisions must be recorded in the Record of Amendments Log Sheet, which is contained in Attachment G of this SESC Plan, and dated red-lined drawings and/or a detailed written description must be appended to the SESC Plan. Inspection Forms must be revised to reflect all amendments. Update the Revision Date and the Version # in the footer of the Report to reflect amendments made.

All SESC Plan Amendments, except minor non-technical revisions, must be approved by the site owner and operator. Any amendments to control measures that involve the practice of engineering must be reviewed, signed, and stamped by a Professional Engineer registered in the State of RI.

The amended SESC plan must be kept on file at the site while construction is ongoing and any modifications must be documented.

Attach a copy of the Amendment Log.

- Refer to Attachment G

SECTION 6: RECORDKEEPING

RIPDES Construction General Permit – Parts III.D, III.G, III.J.3.b.iii, & V.O

It is the site owner and site operator's responsibility to have the following documents available at the construction site and immediately available for RIDEM review upon request:

- A copy of the fully signed and dated SESC Plan, which includes:
 - A copy of the General Location Map
INCLUDED AS ATTACHMENT A
 - A copy of all SESC Site Plans
INCLUDED AS ATTACHMENT B
 - A copy of the RIPDES Construction General Permit (*To save paper and file space, do not include in DEM/CRMC submittal, for operator copy only*)
INCLUDED AS ATTACHMENT C
 - A copy of any regulatory permits (RIDEM Freshwater Wetlands Permit, CRMC Assent, RIDEM Water Quality Certification, RIDEM Groundwater Discharge Permit, RIDEM RIPDES Construction General Permit authorization letter, etc.)
INCLUDED AS ATTACHMENT D
 - The signed and certified NOI form or permit application form (*if required as part of the application, see RIPDES Construction General Permit for applicability*)
INCLUDED AS ATTACHMENT E
 - Completed Inspection Reports w/Completed Corrective Action Logs
INCLUDED AS ATTACHMENT F
 - SESC Plan Amendment Log
INCLUDED AS ATTACHMENT G

SECTION 7: PARTY CERTIFICATIONS

RIPDES Construction General Permit – Part V.G

All parties working at the project site are required to comply with the Soil Erosion and Sediment Control Plan (SESC Plan including SESC Site Plans) for any work that is performed on-site. The site owner, site operator, contractors and sub-contractors are encouraged to advise all employees working on this project of the requirements of the SESC Plan. A copy of the SESC Plan is available for your review at the following location: 20 Goddard Drive, or may be obtained by contacting the site owner or site operator.

The site owner and site operator and each subcontractor engaged in activities at the construction site that could impact stormwater must be identified and sign the following certification statement.

I acknowledge that I have read and understand the terms and conditions of the Soil Erosion and Sediment Control (SESC) Plan for the above designated project and agree to follow the control measures described in the SESC Plan and SESC Site Plans.

Site Owner:

20 Goddard, LLC
10 Greene Street
Providence, RI 02903
401-273-8010 x272

signature/date

Site Operator:

Insert Company or Organization Name
Insert Name & Title
Insert Address
Insert City, State, Zip Code
Insert Telephone Number, Insert Fax/Email

signature/date

Designated Site Inspector:

Insert Company or Organization Name
Insert Name & Title
Insert Address
Insert City, State, Zip Code
Insert Telephone Number, Insert Fax/Email

signature/date

Sub-Contractor SESC Plan Contact:

Garofalo & Associates, Inc.
Samuel Hemenway, PE
85 Corliss Street
Providence, RI 02940
401.273.6000, shemenway@garofaloassociates.com

signature/date

LIST OF ATTACHMENTS

Attachment A - General Location Map

Attachment B - SESC Site Plans

**Attachment C - Copy of RIPDES Construction General Permit and
Authorization to Discharge**

<http://www.dem.ri.gov/programs/benviron/water/permits/swcoord/pdf/cpg092618.pdf>

Attachment D - Copy of Other Regulatory Permits

Attachment E - Copy of RIPDES NOI

<http://www.dem.ri.gov/pubs/regs/regs/water/sms4noi.pdf>

Attachment F - Inspection Reports w/ Corrective Action Log

Attachment G - SESC Plan Amendment Log

SESC Plan Inspection Report

Project Information			
Name			
Location			
DEM Permit No.			
Site Owner	Name	Phone	Email
Site Operator	Name	Phone	Email
Inspection Information			
Inspector Name	Name	Phone	Email
Inspection Date		Start/End Time	
Inspection Type <input type="checkbox"/> Weekly <input type="checkbox"/> Pre-storm event <input type="checkbox"/> During storm event <input type="checkbox"/> Post-storm event <input type="checkbox"/> Other			
Weather Information			
Last Rain Event Date: Duration (hrs): Approximate Rainfall (in):			
Rain Gauge Location & Source:			
Weather at time of this inspection:			

Check statement that applies then sign and date below:

I, as the designated Inspector, certify that this site has been inspected as required by regulation and I have determined that maintenance and corrective actions are not required at this time.

I, as the designated Inspector, certify that this site has been inspected as required by regulation and I have made the determination that the site requires corrective actions. The required corrective actions are noted within this inspection report.

Inspector:	Print Name	Signature	Date
<p>The Site Operator acknowledges by his/her signature, the receipt of this SESC Plan inspection report and its findings. He/she acknowledges that all recommended corrective actions must be completed and documentation of all such corrective actions must be made in this inspection report per applicable regulations.</p>			
Operator:	Print Name	Signature	Date

Site-specific Control Measures

Number the structural and non-structural stormwater control measures identified in the SESC Plan and on the SESC Site Plans and list them below (add as necessary). Bring a copy of this inspection form and any applicable SESC Site Plans with you during your inspections. This list will assist you to inspect all control measures at your site.

FILL THIS TABLE USING THE SESC PLAN TABLES 2.11 & 3.12.

	Location/Station	Control Measure Description	Installed & Operating Properly?	Assoc. Photo/ Figure #	Corrective Action Needed (Yes or No; if 'Yes', please detail action required)
1	Example 1: Eastern Parcel – Slope No. 4 Adjacent to I-95. Straw Wattles	Straw Wattle. Section Six, Sediment Control Measures, Straw Wattles, Compost Tubes and Fiber Rolls - <i>RI SESC Handbook</i> .	<input type="checkbox"/> Yes <input type="checkbox"/> No		
2	Example 2: Western Parcel – Green Street Construction Entrance	Stone Stabilized Pad. Section Six: Sediment Control Measures – Construction Entrances – <i>RI SESC Handbook</i> .	<input type="checkbox"/> Yes <input type="checkbox"/> No		
3	Example 3: Hospital Main Footings – Excavation Area – SESC Site Plan Sheet No. 3.	Pump Intake Protection Using Stone Filled Sump with Standpipe. Section Six: Sediment Control Measures, Pump Intake Protection, <i>RI SESC Handbook</i> .	<input type="checkbox"/> Yes <input type="checkbox"/> No		
4	Example 4: Bridge Abutment Construction Southbound Bridge Abutment, Bridge No. 244 – SESC Site Plan Sheet No. 18.	Prefabricated Concrete Washout Container with Ramp. Used to contain concrete washout during concrete pouring operations. Section Three: Pollution Prevention and Good Housekeeping, Concrete Washouts, <i>RI SESC Handbook</i> .	<input type="checkbox"/> Yes <input type="checkbox"/> No		
5	INSERT TEXT	INSERT TEXT	<input type="checkbox"/> Yes <input type="checkbox"/> No		
6	Attention Operator:	You must modify this inspection form as the project progresses, control measure locations change, and amendments to the SESC Plan are instituted in the field.	<input type="checkbox"/> Yes <input type="checkbox"/> No		
7			<input type="checkbox"/> Yes <input type="checkbox"/> No		
8			<input type="checkbox"/> Yes <input type="checkbox"/> No		

PROJECT:

INSPECTION DATE:

	Location/Station	Control Measure Description	Installed & Operating Properly?	Assoc. Photo/ Figure #	Corrective Action Needed (Yes or No; if 'Yes', please detail action required)
9			<input type="checkbox"/> Yes <input type="checkbox"/> No		
10			<input type="checkbox"/> Yes <input type="checkbox"/> No		
11			<input type="checkbox"/> Yes <input type="checkbox"/> No		
12			<input type="checkbox"/> Yes <input type="checkbox"/> No		
13			<input type="checkbox"/> Yes <input type="checkbox"/> No		
14			<input type="checkbox"/> Yes <input type="checkbox"/> No		
15			<input type="checkbox"/> Yes <input type="checkbox"/> No		
16			<input type="checkbox"/> Yes <input type="checkbox"/> No		
17			<input type="checkbox"/> Yes <input type="checkbox"/> No		
18			<input type="checkbox"/> Yes <input type="checkbox"/> No		
19			<input type="checkbox"/> Yes <input type="checkbox"/> No		
20			<input type="checkbox"/> Yes <input type="checkbox"/> No		
21			<input type="checkbox"/> Yes <input type="checkbox"/> No		
22			<input type="checkbox"/> Yes <input type="checkbox"/> No		
23			<input type="checkbox"/> Yes <input type="checkbox"/> No		
24			<input type="checkbox"/> Yes <input type="checkbox"/> No		

PROJECT:

INSPECTION DATE:

	Location/Station	Control Measure Description	Installed & Operating Properly?	Assoc. Photo/ Figure #	Corrective Action Needed (Yes or No; if 'Yes', please detail action required)
25			<input type="checkbox"/> Yes <input type="checkbox"/> No		
26			<input type="checkbox"/> Yes <input type="checkbox"/> No		
27			<input type="checkbox"/> Yes <input type="checkbox"/> No		
28			<input type="checkbox"/> Yes <input type="checkbox"/> No		
29			<input type="checkbox"/> Yes <input type="checkbox"/> No		
30			<input type="checkbox"/> Yes <input type="checkbox"/> No		

(add more as necessary)

General Site Issues

Below are some general site issues that should be assessed during inspections. Please **customize** this list as needed for conditions at the site.

	Compliance Question		Assoc. Photo/ Figure #	Corrective Action Needed (If 'Yes', please detail action required and include location/station)
1	Have all control measures been installed as specified in the RISESC Handbook and prior to any earth disturbing activities?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
2	Are appropriate limits of disturbance (LOD) established?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
3	Are controls that limit runoff from exposed soils by diverting, retaining, or detaining flows (such as check dams, sediment basins, etc.) in place?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
4	Are all temporary conveyance practices installed correctly and functioning as designed?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
5	Has maintenance been performed as required to ensure continued proper function of all temporary conveyances practices?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
6	Were all exposed soils seeded by October 15 th ?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
7	Have soils been stabilized where earth disturbance activities have permanently or temporarily ceased on any portion of the site and will not resume for more than 14 days?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
8	In instances where adequate vegetative stabilization was not established by November 15 th , have non-vegetative erosion control measures must be employed?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
9	If work is to continue from October 15 th through April 15 th , are steps taken to ensure that only the day's work area will be exposed and all erodible soil is stabilized within 5 working days?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
10	Have inlet protection measures (such as fabric drop inlet protection, curb drop inlet protection, etc.) been properly installed?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
11	Has the operator cleaned and maintained inlet protection measures when needed?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
12	Has the operator removed accumulated sediment adjacent to inlet protection measures within 24 hours of detection?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		

	Compliance Question		Assoc. Photo/ Figure #	Corrective Action Needed (If 'Yes', please detail action required and include location/station)
13	Has the operator properly installed outlet protection (such as riprap, turf mats, etc.) at all temporary and permanent discharge points?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
14	Are all outlet protection measures functioning properly in order to reduce discharge velocity, promote infiltration, and eliminate scour?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
15	Have all discharge points been inspected to ensure the prevention of scouring and channel erosion?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
16	Have sediment controls been installed along perimeter areas that will receive stormwater from earth disturbing activities?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
17	Is the operator maintaining sediment controls in accordance with the requirements in the <i>RI SESC Handbook</i> ?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
18	Have temporary sediment barriers been installed around permanent infiltration areas (such as bioretention areas, infiltration basins, etc.)?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
19	Have staging areas and equipment routing been implemented to avoid compaction where permanent infiltration areas will be located?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
20	Are surface outlet structures (such as skimmers, siphons, etc.) installed for each temporary sediment basin? [Exception: frozen conditions]	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
21	Have all temporary sediment basins or traps been inspected and maintained as required to ensure proper function?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
22	Does the project include the use of polymers, flocculants, or other chemicals to control erosion, sedimentation, or runoff from the site?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
23	Are all chemicals being managed in accordance with Appendix J of the <i>RI SESC Handbook</i> and current best management practices?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
24	Has the site operator taken steps to prohibit the following pollutant discharges on the site?			
a	Contaminated groundwater.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		

	Compliance Question		Assoc. Photo/ Figure #	Corrective Action Needed (If 'Yes', please detail action required and include location/station)
b	Wastewater from washout of concrete; unless properly contained, managed, and disposed of.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
c	Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction products.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
d	Fuels, oils, or other pollutants used in vehicle and equipment operation and maintenance.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
e	Soaps or solvents used in vehicle and equipment washing.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
f	Toxic or hazardous substances from a spill or other release.	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
25	Is the operator using properly constructed entrances/exits to the site so sediment removal occurs prior to vehicles exiting?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
26	If needed, are additional controls (such as rumble strips, rattle plates, etc.) in place to remove sediment from tires prior to exiting?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
27	Is sediment track-out being removed by the end of the same workday in which it occurs (via sweeping, shoveling, or vacuuming)?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
28	Are all wastes generated at the site being managed and properly disposed of by the end of each workday?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
29	Are all chemicals and hazardous waste materials stored properly in covered areas and surrounded by containment control systems?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
30	Has the operator established highly visible locations for the storage of spill prevention and control equipment on the construction site?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
31	Are allowable non-stormwater discharges being managed properly with adequate controls?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
32	Is the site operator properly managing groundwater or stormwater that is removed from excavations, trenches, or similar points of accumulation?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
33	Are proper procedures and controls in place for the storage of materials that may discharge pollutants if	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		

	Compliance Question		Assoc. Photo/ Figure #	Corrective Action Needed (If 'Yes', please detail action required and include location/station)
	exposed to stormwater?			
	Are stockpiles located within the limits of disturbance?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	Are stockpiles being protected from contact with stormwater using a temporary sediment barrier?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	Where needed, has cover or appropriate temporary vegetative or structural stabilization been utilized for stockpiles?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	Is the operator effectively managing the generation of dust through the use of water, chemicals, or minimization of exposed soil?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	Are designated washout areas (such as wheel washing stations, washout for concrete, paint, stucco, etc.) clearly marked on the site?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	Are vehicle fueling and maintenance areas properly located to prevent pollutants from impacting stormwater and sensitive receptors?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> N/A		
	(Other)			

(add more as necessary)

PROJECT:

INSPECTION DATE:

General Field Comments:

PROJECT:

INSPECTION DATE:

Photos:

(Associated photos – each photo should be dated and have a unique identification # and written description indicating where it is located within the project area. If a close up photo is required, it should be preceded with a photo including both the detail area and some type of visible fixed reference point. Photos should be annotated with Station numbers and other identifying information where needed.)

Photo #: (insert Photo here)	Station:
	Description:

Photo #: (insert Photo here)	Station:
	Description:

Photo #: (insert Photo here)	Station:
	Description:

Photo #: (insert Photo here)	Station:
	Description:

Photo #: (insert Photo here)	Station:
	Description:

Photo #: (insert Photo here)	Station:
	Description:

(add more as necessary)

PROJECT:

Amendment Log

TO BE FILLED OUT BY SITE OPERATOR

Describe amendment(s) to be made to the SESC Plan, the date, and the person/title making the amendment. ALL amendments must be approved by the Site Owner.

#	Date	Description of Amendment	Amended by: Person/Title	Site Owner Must Initial
1				
2				
3				
4				
5				
6				
7				
8				
9				
10				

Add more lines/pages as necessary
